



Riprap



Trash Excavation Area 3



Ballfield Embankment


### Major Milestone Completed/Underway

- » Finished trash excavation in area 2
- » Continued ballfield embankment
- » Continued cut to fill operations
- » Continued concrete and asphalt removals
- » Finished embankment for concessions building
- » Continued trash excavations in area 3
- » Completed riprap from STA 20+00 to 23+00
- » Excavated for riprap from STA 23+00 to 28+00
- » Completed abatement of RACS area 6 & 7

### Upcoming Work

- » Continue cut to fill areas
- » Continue riverbank stabilization
- » Continue ballfield embankment
- » Continue trash excavation
- » Continue river walk asphalt/concrete removals
- » Start underground utilities
- » Continue northeast embankment

Time to Substantial Completion  
Original Contract Calendar Days: 341  
Calendar Days Charged to Date: 147  
Remaining Contract Calendar Days: 194

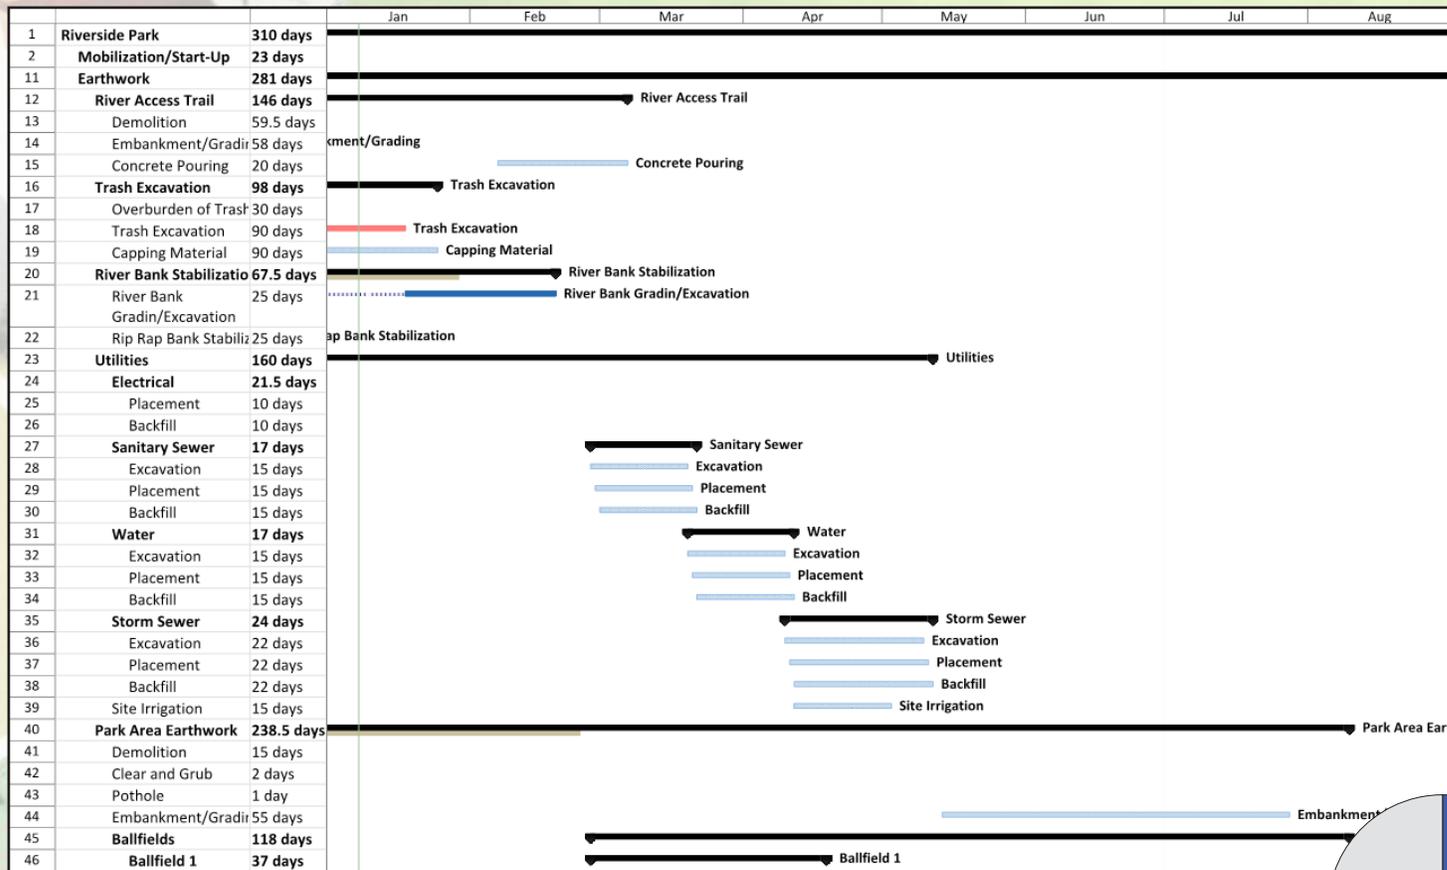

Contract Value: \$10,146,980  
Adjusted Contract Value: \$10,146,980  
Work Complete: \$4,331,082

43% Complete

