



Area II Embankment



Concessions Foundation



Riprap


Major Milestone Completed/Underway

- » Finished trash excavation in area 3
- » Continued ball field embankment
- » Continued cut to fill operations
- » Finished concrete and asphalt removals
- » Finished structure excavation for concessions building foundations
- » Finished structure excavation for concrete amphitheater seating in ballfields
- » Completed subgrade prep for southwest river trail
- » Completed installation of riprap
- » Completed embankment for north parking lot


Upcoming Work

- » Finish riverbank stabilization
- » Finish ball field embankment/rough grade
- » Continue river walk subgrade prep
- » Start underground utilities (water and sewer)
- » Finish capping of trash areas
- » Pour concrete foundations and sidewalks
- » Start fencing operations

Time to Substantial Completion
Original Contract Calendar Days: 341
Calendar Days Charged to Date: 178
Remaining Contract Calendar Days: 163

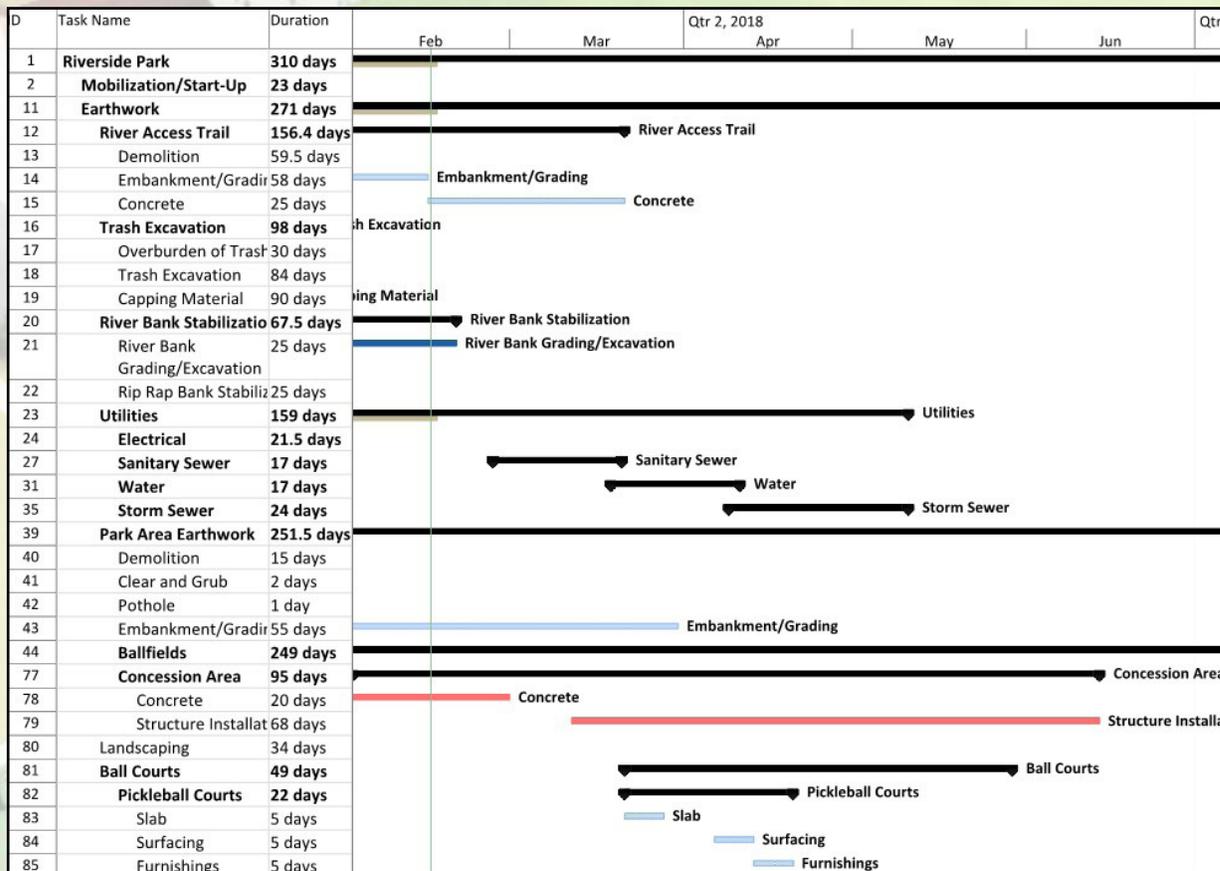

47% Complete

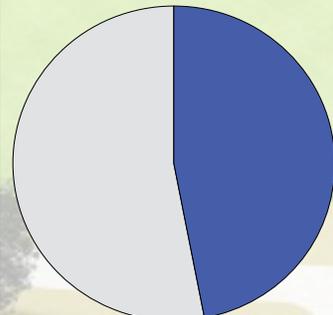

Contract Value: \$10,146,980
Adjusted Contract Value: \$11,151,035
Work Complete: \$4,807,466
