

City of Evans Riverside Park Restoration Project

Monthly Report: November 2017



Riprap



Embankment



Trash Excavation


Major Milestone Completed/Underway

- » Finished trash excavation in area 1
- » Finished electrical mainline runs from concessions building to ball fields
- » Continued ballfield embankment
- » Continued cut to fill operations
- » Continued concrete and asphalt removals
- » Finished south parking lot embankment/grading
- » Started embankment for concessions building and playground area
- » Started trash excavations in areas 2 and 3
- » Completed riprap from STA 11+00 to 20+00
- » Completed 2 storm drain culverts
- » Completed abatement of RACS areas 1-5

Upcoming Work

- » Continue cut to fill areas
- » Continue riverbank stabilization
- » Continue ballfield embankment
- » Continue trash excavation
- » Continue river walk asphalt/concrete removals
- » Start underground utilities
- » Continue northeast embankment

Time to Substantial Completion
 Original Contract Calendar Days: 341
 Calendar Days Charged to Date: 116
 Remaining Contract Calendar Days: 225

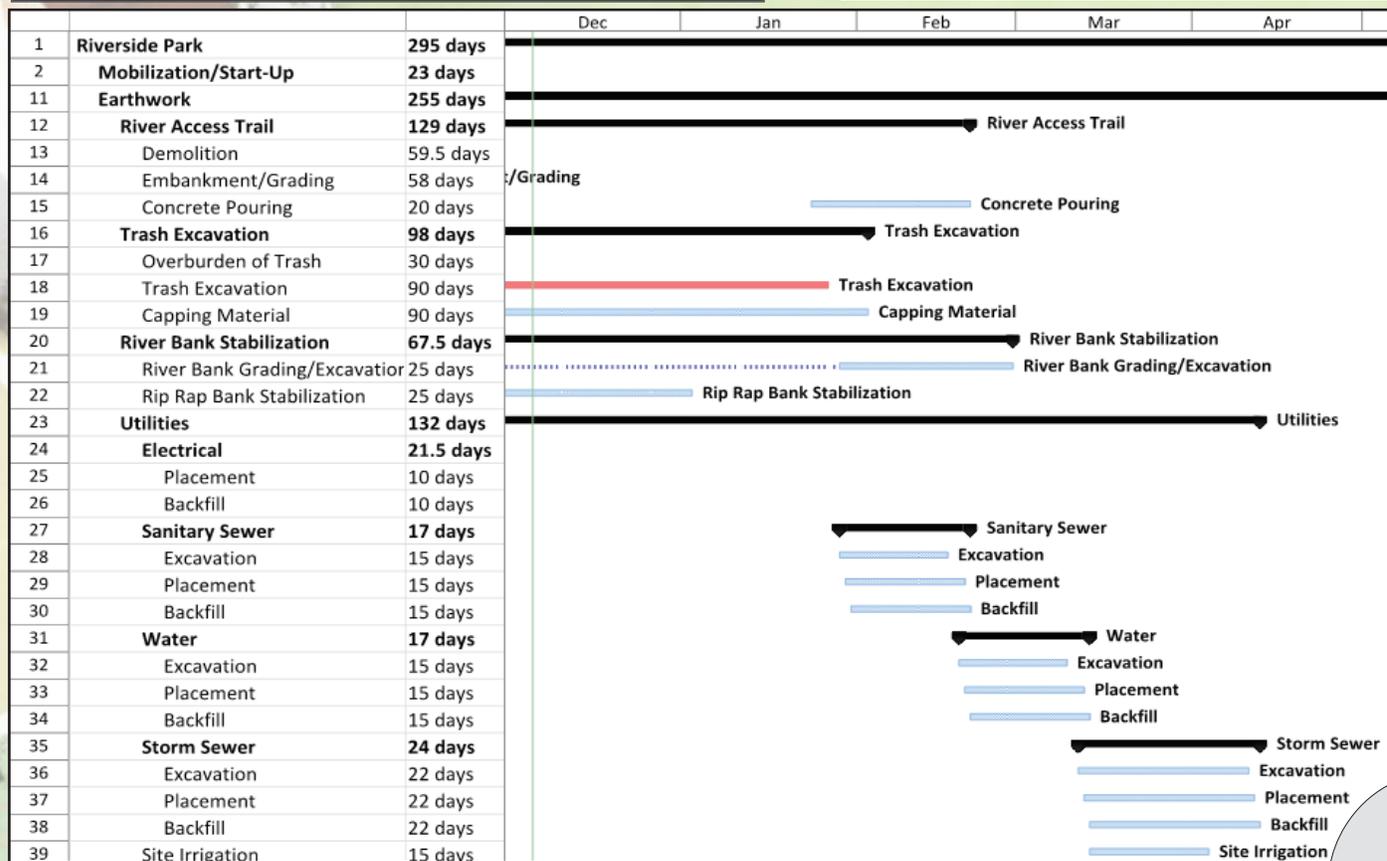

Contract Value: \$10,146,980
 Adjusted Contract Value: \$10,146,980
 Work Complete: \$3,429,694

34% Complete

