

City of Evans Riverside Park Restoration Project

Monthly Report: October 2017



Ball Field Embankment



Pond Overflow Culvert




Trash Excavation Area 1

Major Milestone Completed/Underway

- » Continued trash excavation and haul operations
- » Started electrical mainline runs
- » Continued ball field embankment
- » Continued cut to fill operations
- » Continued concrete and asphalt removals
- » Started parking lot embankment/grading
- » Started placing riprap
- » Completed 2 storm drain culverts

Upcoming Work

- » Continue cut to fill areas
- » Continue riverbank stabilization
- » Continue ball field embankment
- » Continue trash excavation
- » Continue north/south parking lot grading
- » Continue riverwalk asphalt/concrete removals
- » Start underground utilities

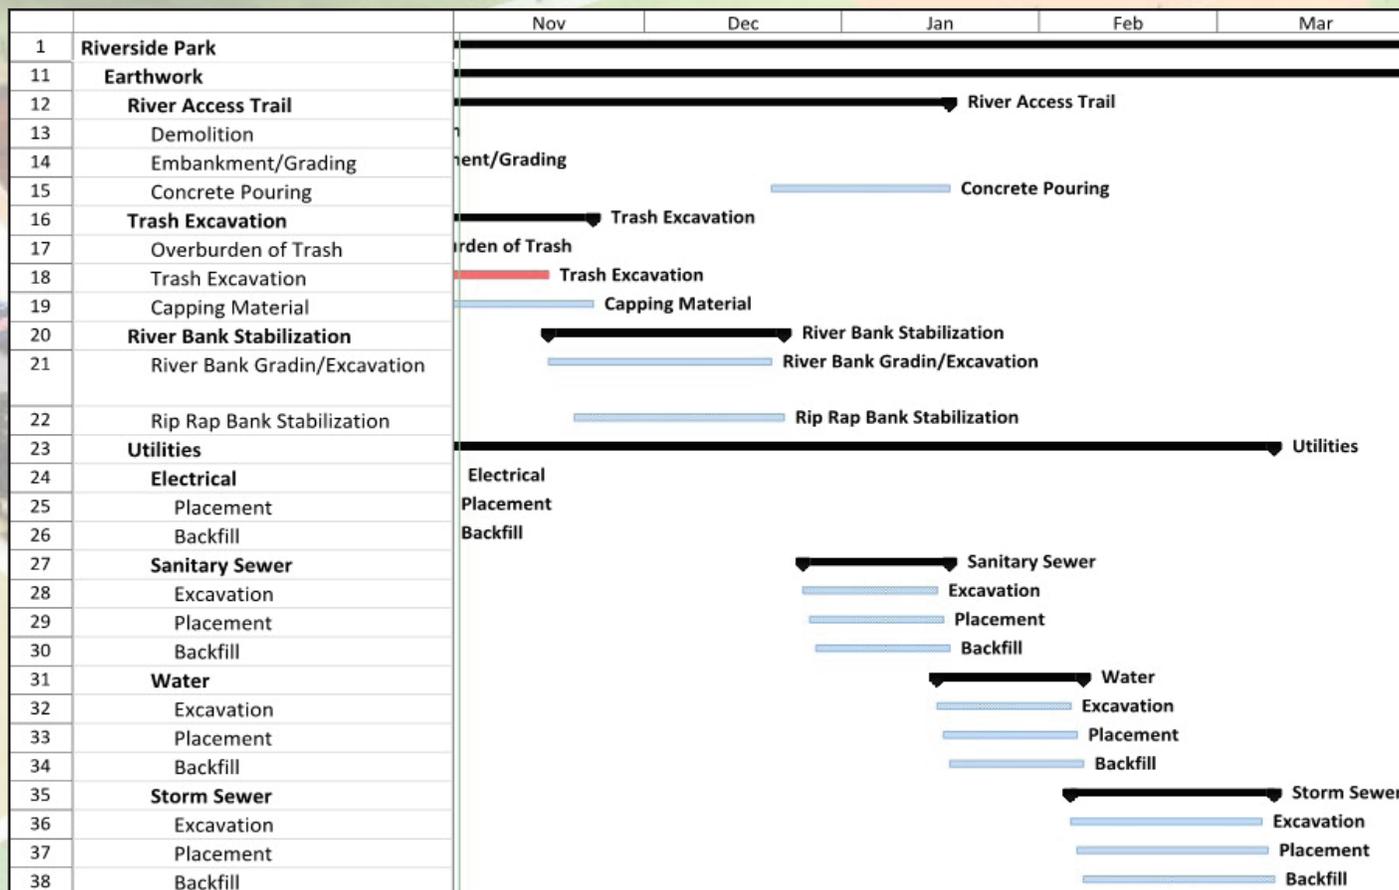

Time to Substantial Completion
 Original Contract Calendar Days: 341
 Calendar Days Charged to Date: 86
 Remaining Contract Calendar Days: 255

Contract Value: \$10,146,980
 Adjusted Contract Value: \$10,146,980
 Work Complete: \$2,116,750

21% Complete

