

Project Weekly Report

PROJECT: Riverside Park Flood Restoration Project

FROM: George Latour, Ditesco
Justin Schaller, Ditesco

DATE: June 30, 2018 to July 6, 2018


Sitework:

- Continued placing irrigation
- Started placing sod in north fields
- Continued pouring curb and gutter in north parking lot
- Finished placing roof trusses on the concession building
- Continued placing ballfield mow strips
- Continued concrete for stadium seating
- Continued placing infield mix on north fields
- Continued fencing operations
- Continued working on irrigation pond parking lot
- Started re-lamping ballfield lights



Other:

- Additional scope approved by Council

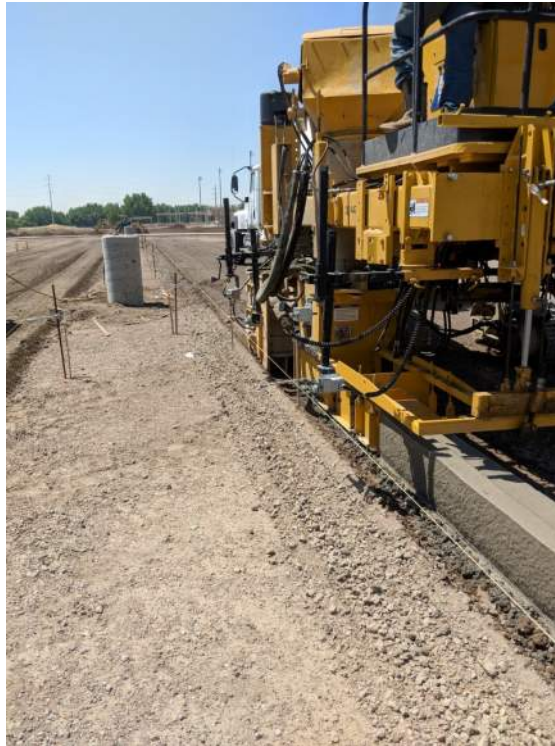

Upcoming work:

- Finish shade structure steel
- Start roof panels on concession building
- Continue concrete sidewalks and curb/gutter
- Continue center ballfield concrete
- Continue site irrigation
- Start playground surfacing
- Continue electrical in concession building
- Finish ballfield sod
- Finish Musco light lamps and aiming

