



Ballfield Plaza



Concrete V-Pans




Curb & Gutter Repair

Major Milestones Completed/Underway

- » Finished planting trees
- » Finished outstanding playground items
- » Finished roof soffit at concession building
- » Finished rough in for plumbing and electrical in building
- » Finished plumbing trim out in concession building
- » Finished ballfield fencing
- » Finished installing remaining sod
- » Finished site irrigation
- » Finished remaining shade structures
- » Finished all native seeding
- » Finished remaining CMU at pavilion columns
- » Completed south entrance curb and gutter concrete repairs
- » Continued painting and finishes in concession building
- » Repaired infield mix
- » Installed all site amenities
- » Installed remaining park signage
- » Started working on punchlist items

Upcoming Work

- » Finish grading/seeding around concrete v-pans
- » Finish site electrical
- » Finish concession building
- » Finish landscaping
- » Finish laydown yard improvements
- » Final acceptance and grand opening

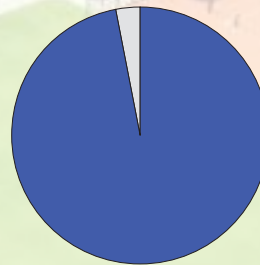

97% Complete

Contract Value: \$10,146,980
Adjusted Contract Value: \$11,741,581
Work Complete: \$11,424,812

Time to Final Completion
Original Contract Calendar Days: 420
Revised Contract Calendar Days: 450
Calendar Days Charged to Date: 420
Remaining Contract Calendar Days: 30

