

Project Weekly Report


PROJECT: Riverside Park Flood Restoration Project

FROM: George Latour, Ditesco
Justin Schaller, Ditesco

DATE: February 15, 2018 to March 3, 2018

Sitework:

- Continued Turf Reinforcement Mat (TRM) for riverbank stabilization
- Completed concession building foundation walls
- Set ballfield fencing posts in reinforced concrete
- Continued concrete/asphalt crushing operations
- Test run on concrete slip machine for 10' sidewalk pours
- Poured river access concrete walk
- Started drilling caissons for shade structures in ballfields
- Started forming foundations for amphitheater seating in ballfields
- Fine-grade for concrete walkways
- Finished subgrade in ballfield 3
- Continued underground electrical work in concessions building
- Started 8" waterline
- Started placing topsoil in area 1

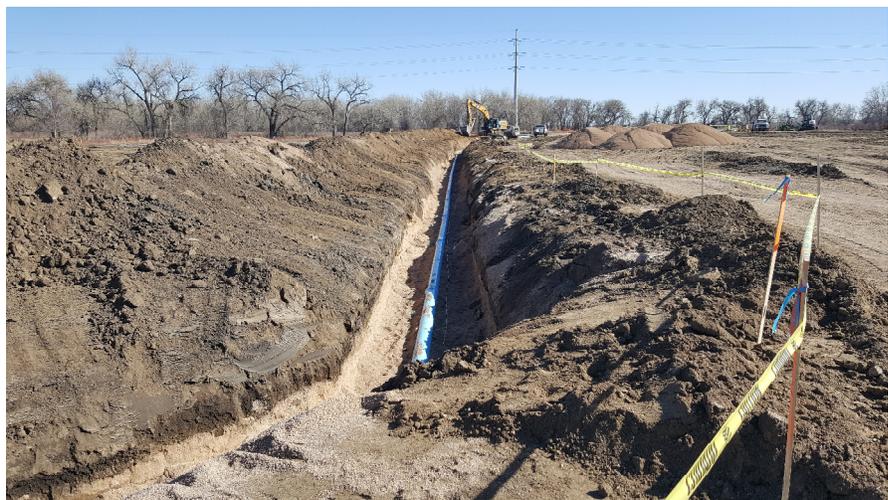

- Completed capping areas in 2 and 3

Other:

- Snow delays this week



Upcoming work:

- Continue TRM and topsoil
- Start harvesting willows
- Continue underground waterline
- Finish subgrade prep for concrete walkways
- Continue center of ballfield foundations
- Continue fencing operations
- Verify capping areas
- Start concrete sidewalks
- Continue crushing operations

