



Climbing Wall



Soil Amendment



Tree Planting


Major Milestones Completed/Underway

- » Completed top soil placement on riverbank area
- » Started placing soil amendment on riverbank area
- » Started planting non-irrigated trees on east side of project
- » Started planting willow stakes
- » Completed climbing wall foundation and retaining wall
- » Continued concrete sidewalks
- » Completed ball field amphitheater seating foundations
- » Continued subgrade prep for walk paths
- » Completed underground plumbing and electrical in building
- » Started setting outfield fence posts
- » Completed backstop fence posts
- » Finished topsoil placement in ball field sod areas
- » Started backfill for ball field amphitheater foundations
- » Removed final shade structure
- » Started topsoil placement in detention ponds

Upcoming Work

- » Start seeding operations for riverbank area
- » Continue backfilling foundations for ball field seating
- » Continue concrete sidewalks
- » Continue fencing operations
- » Start sanitary sewer installation
- » Start concession building structure
- » Complete storm drain culverts
- » Start concrete curb & gutter
- » Start irrigation mainline
- » Start playground equipment installation
- » Continue planting trees

59% Complete

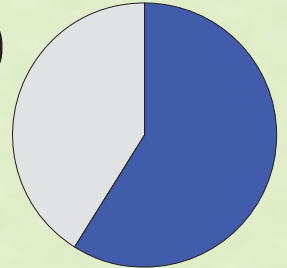

Time to Substantial Completion

Original Contract Calendar Days: 341
Calendar Days Charged to Date: 267
Remaining Contract Calendar Days: 74

Contract Value: \$10,146,980

Adjusted Contract Value: \$11,264,699

Work Complete: \$6,645,406

