

Crushing Operations



Concessions Foundation




River Access Walk

Major Milestone Completed/Underway


- » Completed ball field embankment
- » Completed capping material placement
- » Completed concession building foundation
- » Continued subgrade prep for walk paths
- » Started concrete/asphalt crushing operations
- » Started Turf Reinforcement Mat installation
- » Started topsoil operations for riverbank stabilization sections
- » Started work on ball field fencing
- » Started underground water main

Upcoming Work

- » Finish riverbank stabilization
- » Finish river walk subgrade prep
- » Finish crushing operations
- » Continue concrete foundations for ball field seating
- » Pour concrete sidewalks
- » Continue fencing operations
- » Start sanitary sewer installation
- » Start electrical/plumbing rough in for concession building
- » Start concession building structure

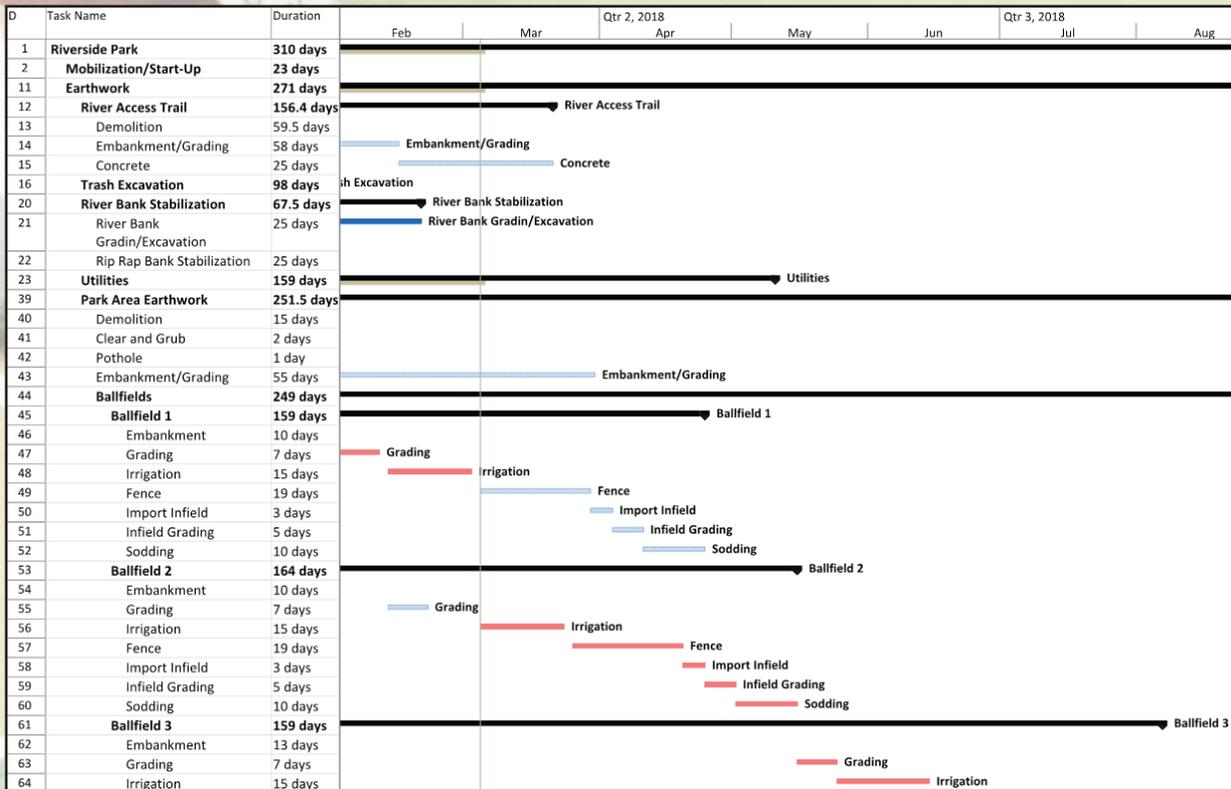

51% Complete

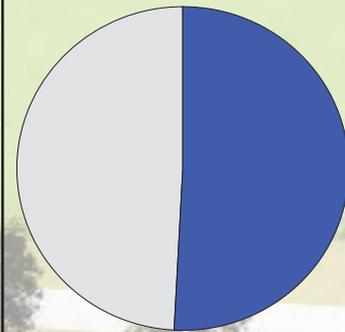

Time to Substantial Completion
Original Contract Calendar Days: 341
Calendar Days Charged to Date: 206
Remaining Contract Calendar Days: 135

Contract Value: \$10,146,980
Adjusted Contract Value: \$11,151,035
Work Complete: \$5,237,503
