




Concession Building



Seating Foundation

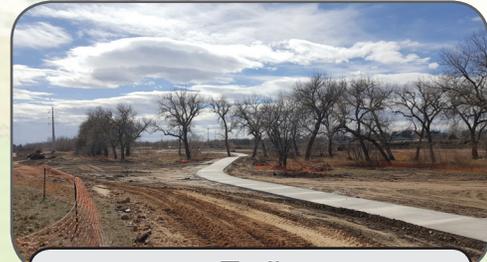


Trail

Major Milestone Completed/Underway

- » Continued top soil placement on riverbank area
- » Completed concession building foundation backfill
- » Continued concrete sidewalks
- » Continued ball field amphitheater seating foundations
- » Continued subgrade prep for walk paths
- » Completed concrete/asphalt crushing operations
- » Completed Turf Reinforcement Mat installation
- » Completed underground water main
- » Completed underground electrical in concessions building
- » Started unground plumbing in electrical building


Upcoming Work

- » Complete top soil placement on riverbank area
- » Start seeding operations for riverbank area
- » Continue concrete foundations for ball field seating
- » Continue concrete sidewalks
- » Continue fencing operations
- » Start sanitary sewer installation
- » Finish plumbing rough in for concession building
- » Start concession building structure
- » Complete storm drain culverts
- » Start concrete curb & gutter
- » Start irrigation mainline

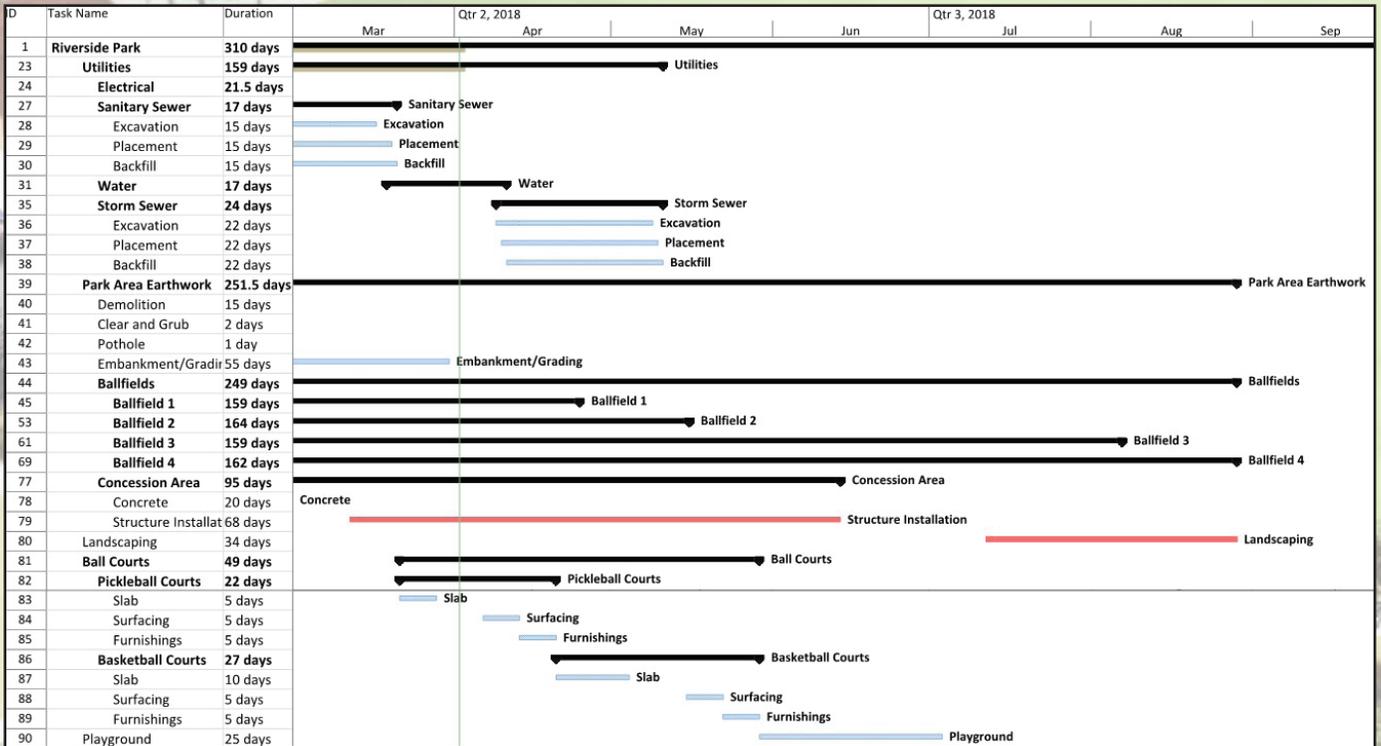

Time to Substantial Completion
Original Contract Calendar Days: 341
Calendar Days Charged to Date: 237
Remaining Contract Calendar Days: 104

Contract Value: \$10,146,980
Adjusted Contract Value: \$11,151,035
Work Complete: \$6,149,680

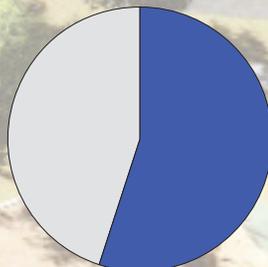

55% Complete
