


Climbing Wall



Riverbank

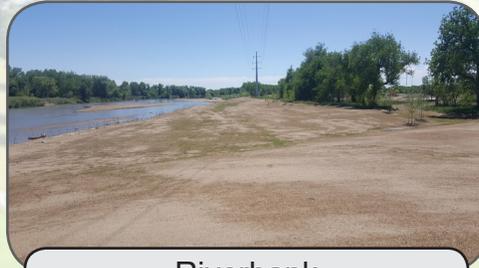

Ballfield Structures



## Major Milestones Completed/Underway

- » Started seeding operations for riverbank area
- » Finished planting non-irrigated trees on east side of project
- » Finished planting willow stakes
- » Finished playground equipment and started climbing wall
- » Continued concrete sidewalks
- » Started concrete curb and gutter
- » Continued subgrade prep for walk paths
- » Started CMU walls at concession building
- » Started rough in for plumbing and electrical in building
- » Finished setting outfield fence posts
- » Started soil amendment in detention ponds and ballfields
- » Started pumphouse repair and installed new irrigation pump
- » Started site irrigation
- » Started new shade structures
- » Finished sanitary sewer

## Upcoming Work

- » Continued soil amendment and seeding operations
- » Finish shade structures
- » Continue concrete in center of ballfields
- » Finish concrete sidewalks
- » Continue fencing operations
- » Continue concession building
- » Continue concrete curb and gutter
- » Finish irrigation
- » Finish playground area
- » Continue landscaping

72% Complete

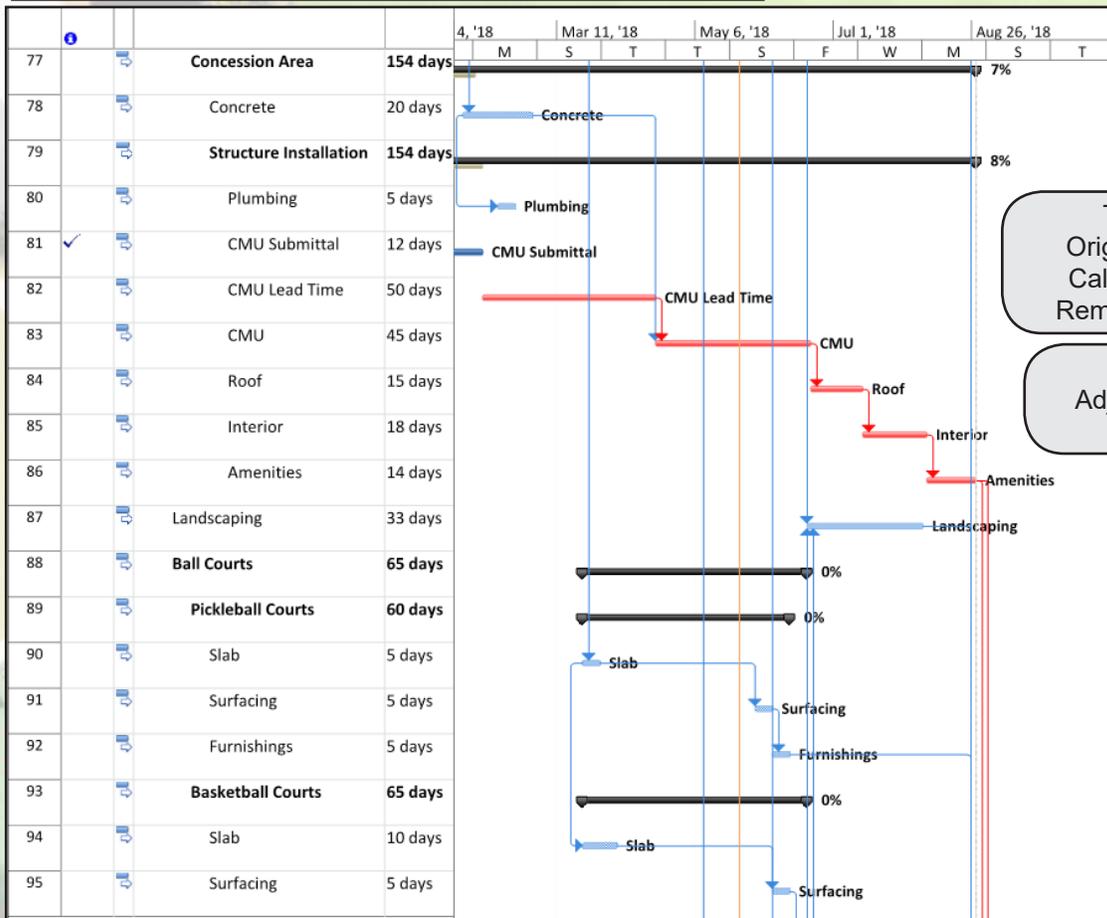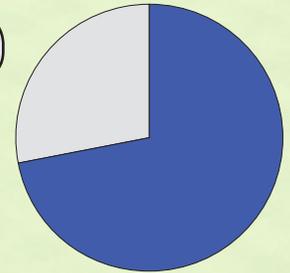

Time to Substantial Completion  
Original Contract Calendar Days: 341  
Calendar Days Charged to Date: 298  
Remaining Contract Calendar Days: 43

Contract Value: \$10,146,980  
Adjusted Contract Value: \$11,264,699  
Work Complete: \$8,076,179
